

Blygold

Project:
The Galleria
2244 East Sunrise Blvd
Fort Lauderdale, FL 33304
Contact: Mr. C. W. Greene



Trane
300 Northpoint Parkway Suite 301
West Palm Beach, FL 33407
Contact: Mr. M. Lansing

Start of the project : February 5th 2007
End of the project : February 9th 2007

Specification of work: Deoxidize and applying the Blygold case coating system on the outside of the air handling unit # 7 including the hood and the roof.

Brygold

Detailed description of work

Start of activities

Technical service of the building shuts off the air handling unit.
Check if the situation meets the working descriptions (as in the quotation), incl. the air handling unit references. (Air handling unit # 7 with hurricane damage on the new roof)
Bring in the equipment and material needed.
Place wood around the air handler to protect the roof.



Check external casing.

Remove through sanding the loose paint and oxidation



Remove the dust after sanding.

Blygold

Blygold Coating system


Apply the Blygold primer Refamac 3509.



Take in account enough drying time.
Apply the Blygold second layer Refamac 3510.




Take in account enough drying time.
Apply the top layer color code RAL 7032.

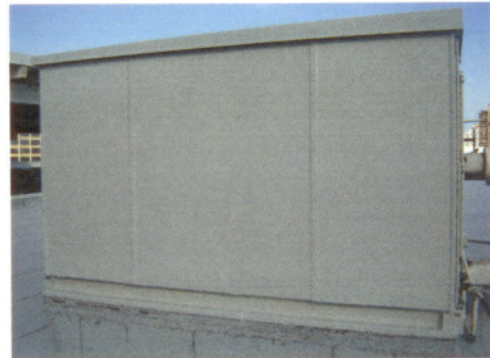

Blygold

Closing activities

Remove all Blygold equipment.

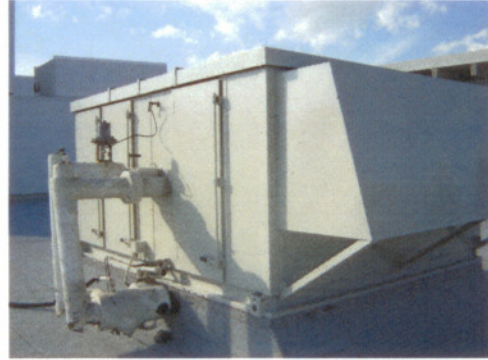

All Blygold equipment will be transported to our Blygold facility in Florida.
Clean the location.
Technical service of the building will do a final inspection and turn on the air handling unit.

I agree that all work mentioned above has been performed to our expectations and satisfaction.

Fort Lauderdale, February 12, 2007.

Galleria Fort Lauderdale
Central Plant Supervisor



Charles W. Greene
